


R-2206 GASTON, LINCOLN & CATAWBA COUNTIES

PROJECT
BREAKDOWN
MAP

NC-16 RELOCATION

PROJECT SCHEDULES AND COSTS ARE ACCURATE AS OF DATE SHOWN

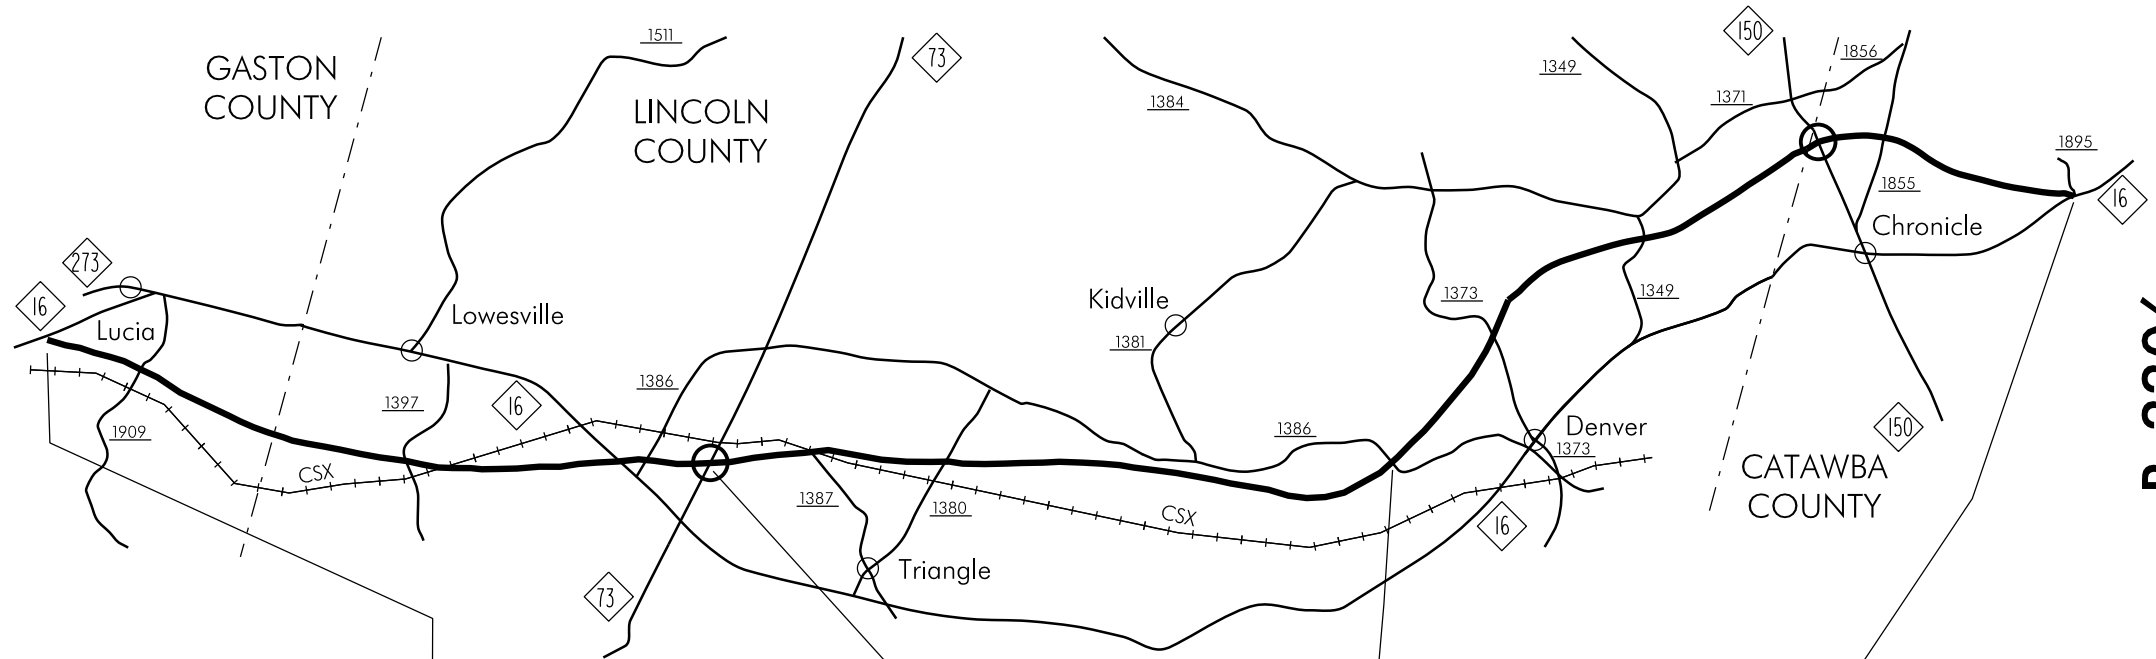

R-2206

	COMPLETE	COMPLETE	COMPLETE	LET	COMPLETE	LET
I.D. NO. / D.S.R. NO.	R-2206 A	R-2206 AA	R-2206 B	R-2206 BA	R-2206 C	R-2206 CA
STATE PROJECT NO. (P.E.)	8.183050 I	8.183050 I	8.183050 I	8.183050 I	8.183050 I	8.183050 I
PROJECT ENGINEER	J. MOORE	J. MOORE	BRUTON	J. MOORE	J. MOORE	J. MOORE
PROJECT DESCRIPTION	NC 16 S.OF LUCIA TO NC 73	NC 16 S.OF LUCIA TO NC 73	NC 16 FROM NC 73 TO SR 1386	NC 16 FROM NC 73 TO SR 1386	NC 16 FROM SR 1386 TO SR 1895	NC 16 FROM SR 1386 TO SR 1895
COUNTY / DIVISION	GASTON & LINCOLN / DIV. 12	GASTON & LINCOLN / DIV. 12	GASTON & LINCOLN / DIV. 12	GASTON & LINCOLN / DIV. 12	LINCOLN & CATAWBA/DIV. 12	LINCOLN & CATAWBA/DIV. 12
LENGTH	5.9 ML.	5.9 ML.	4.7 ML.	4.7 ML.	5.8 ML.	5.8 ML.
TYPE OF CONTRACT	GRADING	PAVING	GRADING	PAVING	GRADING	PAVING
REMARKS						
BEGIN R/W ACQUISITION (T.I.P.)	6-98		10-99		12-02	
BEGIN R/W ACQUISITION (PRODUCTION)						
PROPOSED LETTING (T.I.P.)	7-01	12-04	11-04	9-08	11-04	9-08
PROPOSED LETTING (PRODUCTION)						
EST. COMP. DATE (T.I.P.)	5-05	7-07	4-08	11-11	4-08	11-11
ESTIMATED R/W COST / UTILITY COST	\$ 6,800,000		\$ 5,500,000		\$ 5,500,000	
ESTIMATED CONSTRUCTION COST	\$ 24,500,000	\$ 13,800,000	\$ 21,700,000	\$ 14,200,000	\$ 27,900,000	\$ 15,700,000

